






MAJOR CONSTRUCTION PROJECTS AT A GLANCE

In an effort to keep members of the public informed on major construction projects going on around the city, we prepare and update these “Projects at a Glance” updates. This list is not exhaustive of every project going on, but does highlight the major projects. These projects, often referred to as Capital Improvement Projects (CIP), are primarily large-scale construction projects including road improvement and enhancements, expanded water and wastewater utility projects, major improvements within city parks, and city facility building projects.

TRANSPORTATION PROJECTS	Project Scope	Project Timeline	Project Cost	Current Status
Bagdad Road Reconstruction (RM 1431 to Kettering) 	Bagdad Rd. will be reconstructed with a similar cross section but will include wide outer lanes for bicycles, turn lane improvements at intersections, and sidewalks.	Project construction is set to begin in August 2013 with completion slated for December 2014.	\$4.23M (70% Federal Funding/30% City Funding)	Contract execution and preconstruction meetings are underway.
Cottonwood Creek Trail/New Hope Drive Reconstruction (183A to RM 1431) 	Cottonwood Creek Tr. and New Hope Dr. will be reconstructed from two lanes to four lanes with raised medians, wide outer lanes to accommodate bicycles, sidewalks, and illumination.	Completion scheduled for September 2013.	\$6.055M (Cost Sharing Agreement Between COCP and Williamson Co.)	This project is currently in under construction. Construction of eastbound New Hope lanes and southbound Cottonwood Creek Trail lanes have been completed.

RM 1431 Pass-Through Project

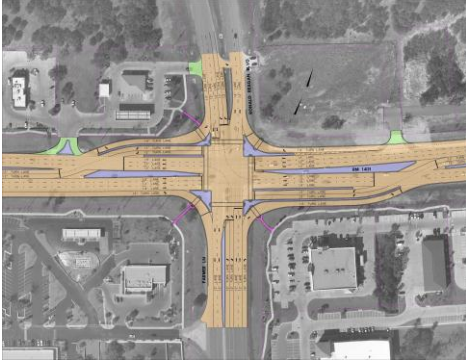

RM 1431 (Whitestone Blvd.) will be reconstructed and widened to a six lane section from Market Street to Sam Bass Rd. The project includes the construction of an innovative intersection known as a Continuous Flow Intersection at RM 1431 & Parmer Ln.

The project is expected to take 18 months to construct.

The City will be responsible for providing initial funding for the \$17M construction budget, 80% of which will be reimbursed by TxDOT based on usage of the completed roadway.

Construction plans are being finalized and construction is scheduled to begin in January 2014.

US 183 at New Hope Turn Lanes



Construction of right turn lanes on northbound and southbound US 183 at New Hope Drive.

Estimated to start construction November 2013.

The project is funded by TxDOT Proposition 12 funds which cover the cost of construction. Design costs will be reimbursed to the City following construction.

The design is being finalized for submission to TxDOT.

US 183 at Walton Way Turn Lanes







Construction of right turn lane on southbound US 183 and an additional left turn lane on northbound US 183 at Walton Way.

Estimated to start construction November 2013.

The project is funded by TxDOT Proposition 12 funds which cover all costs associated with the project.

The design is being finalized for submission to TxDOT.

WATER & WASTEWATER PROJECTS		Project Scope	Project Timeline	Project Cost	Current Status
Cottonwood Creek WW Interceptor 	Project includes the design and construction of a 36" WW line to provide wastewater service to properties along Spanish Oak Creek and Ronald Reagan Blvd. north of RM 1431.	The project is scheduled to be completed in July of 2013.	\$2.05M	Boring operations have been completed and pipe installation is continuing.	
Ronald Reagan Blvd. WW Improvements 	WW line project will provide for 6,000 ft. of 8 and 12" WW line extensions. Project will provide service to areas along Ronald Reagan Blvd. and areas east of 183A, north of New Hope Dr.	The project is slated to be completed August 2013.	\$675,000	Pipe laying operations completed. Testing and site restoration underway.	

CITY FACILITY PROJECTS	Project Scope	Project Timeline	Project Cost	Current Status
<p>Field Operations Building Renovations and Site Improvements</p> 	<p>Includes removal and replacement of roof and wall panels, office reconfiguration, and replacement of exterior and bay doors. Site improvements include additional equipment parking and stock pile storage areas.</p>	<p>Project construction started on 4/1/13 and is slated to be complete by 8/1/13.</p>	<p>\$792,000</p>	<p>Construction of the site improvements have been completed and roof replacement should be completed by the end of June 2013.</p>
<p>Gateway Signage on RM 1431 (Whitestone Blvd.)</p> 	<p>The first COCP Gateway Sign will be constructed on the north side of RM 1431 just west of Sam Bass Rd.</p>	<p>Notice to proceed was issued on June 3, 2013 and the project is scheduled to be completed in August 2013.</p>	<p>\$75,000</p>	<p>Sign production is underway and site preparations should begin in late June 2013.</p>
